


December 2009

Progress Report No. 5

Welcome to the highlights and periodic update of the work underway at Haley's Ditch. We have kept this update short so you can quickly read and see what work is underway and what the next steps will be. If you need more information or have questions please call or write to Cory Smith, Lockheed Martin Communications – 330.796.2038 or 330.256.7209. E-mail [cory.a.smith@lmco.com](mailto:cory.a.smith@lmco.com)

#### Project Work Performed During November

- All soil and sediment that was to be dug up and removed from the Haley's Ditch area has now been removed and taken to licensed off-site facilities
- A total of approximately 27,800 tons of materials have been moved to the American Landfill and approximately 3,500 tons have been moved to the EQ Landfill
- Confirmation samples have been taken from different areas at the site and show that all areas meet cleanup criteria
- All heavy equipment has been cleaned and removed from the site
- Four portable bridges used during the project have been cleaned and removed from the site
- Pump bypass system has been disassembled and removed from the site
- The water treatment equipment was cleaned and removed from the site
- Restoration of the new channel has been completed; fencing has been installed
- Staking of the southern part of the walking trail has been completed

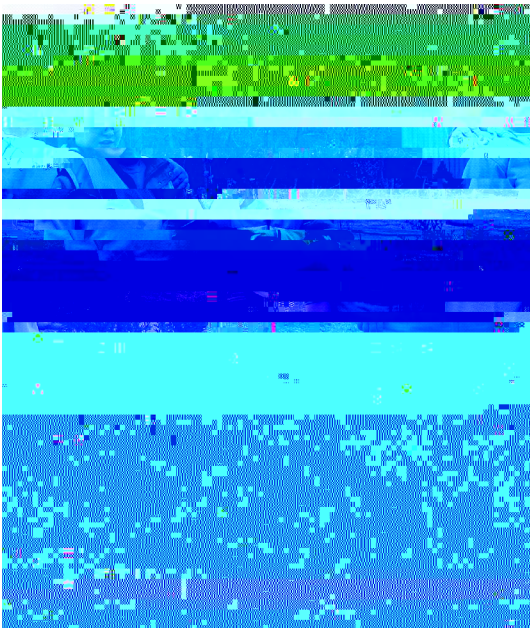

### Work Projected for December

- The final segment of the permanent fence will be completed along the northern portion of the IRG property
- Restoration of the north area will continue as long as weather and suitable working conditions allows

### Health and Safety

- 12,150 man-
